South Bristol Link
Summary Programme for D&B procurement

Mott MacDonald

ID	Task Name	Duration	Start	Finish
1				
2	**Procurement**	**81 wks**	**Fri 22/03/13**	**Thu 09/10/14**
3	Confirm procurement strategy	4 wks	Fri 22/03/13	Thu 18/04/13
4	Prepare OJEU notification	8 wks	Fri 19/04/13	Thu 13/06/13
5	Publish OJEU prequal invitation	0 wks	Thu 13/06/13	Thu 13/06/13
6	Response period	7 wks	Fri 14/06/13	Thu 01/08/13
7	Selct shortlist	2 wks	Fri 02/08/13	Thu 15/08/13
8	Prepare D&B tender documents	24 wks	Fri 16/08/13	Thu 30/01/14
9	Invite tenders	0 wks	Thu 30/01/14	Thu 30/01/14
10	Tender period	12 wks	Fri 31/01/14	Thu 24/04/14
11	Tender evaluation	4 wks	Fri 25/04/14	Thu 22/05/14
12	Cabinet approval to award contract	4 wks	Fri 23/05/14	Thu 19/06/14
13	Appoint contractor	0 wks	Thu 17/07/14	Thu 17/07/14
14	Mobilisation period	12 wks	Fri 18/07/14	Thu 09/10/14
15	**Major Scheme Business Case**	**147.8 wks?**	**Mon 15/10/07**	**Thu 23/09/10**
16	Long list option appraisal	14 wks	Mon 15/10/07	Fri 01/02/08
17	Project Board approval to shortlist	2 wks	Mon 25/08/08	Fri 05/09/08
18	Short list option appraisal	24 wks	Mon 01/09/08	Fri 27/02/09
19	Exec Members approval for consultation	2 wks	Mon 12/10/09	Fri 23/10/09
20	Public consultation (3)	6 wks	Mon 02/11/09	Fri 11/12/09
21	Project Board approval to MSBC	1 wk	Mon 02/03/09	Fri 06/03/09
22	Preferred option design	22 wks	Mon 20/07/09	Fri 18/12/09
23	Preferred option appraisal	18 wks?	Mon 14/09/09	Fri 29/01/10
24	Cabinet approval to announce PR	4 wks	Mon 14/12/09	Fri 22/01/10
25	Announce Preferred Route	0 wks	Fri 22/01/10	Fri 22/01/10
26	Submit MSBC for Programme Entry	0 wks	Fri 26/03/10	Fri 26/03/10
27	OGC Gateway 1	2 wks	Fri 16/07/10	Thu 29/07/10
28	DfT Consideration	26 wks	Fri 26/03/10	Thu 23/09/10
29	DfT Programme Entry	0 wks	Thu 23/09/10	Thu 23/09/10
30	**Planning Application**	**190 wks**	**Thu 30/09/10**	**Thu 03/07/14**
31	Appoint framework consultant	0 wks	Thu 30/09/10	Thu 30/09/10
32	Design and procure GI and Topo surveys	20 wks	Fri 01/10/10	Thu 03/03/11
33	GI and Topo surveys	24 wks	Fri 04/03/11	Thu 18/08/11
34	Scope and plan Environment surveys	12 wks	Fri 01/10/10	Thu 06/01/11
35	Environmental surveys	52 wks	Fri 07/01/11	Thu 19/01/12
36	Identify and prepare traffic survey updates	12 wks	Fri 10/12/10	Thu 17/03/11
37	Traffic surveys	4 wks	Fri 18/03/11	Thu 14/04/11
38	Preliminary scheme design	36 wks	Fri 22/07/11	Thu 12/04/12
39	Environmental Impact Assessment	24 wks	Fri 20/01/12	Thu 05/07/12
40	Transport Assessment	24 wks	Fri 20/01/12	Thu 05/07/12
41	Environmental Statement	32 wks	Fri 20/01/12	Thu 30/08/12
42	Public consultation (4)	6 wks	Fri 06/07/12	Thu 16/08/12
43	OGC Gateway 2	2 wks	Fri 31/08/12	Thu 13/09/12
44	Network Rail Agreement	150 wks	Fri 22/07/11	Thu 03/07/14
45	Cabinet approval to submit Planning Application	4 wks	Fri 14/09/12	Thu 11/10/12
46	Planning submission	0 wks	Thu 11/10/12	Thu 11/10/12
47	**Statutory Process**	**114 wks**	**Fri 25/05/12**	**Thu 14/08/14**
48	Determination period	16 wks	Fri 12/10/12	Thu 14/02/13
49	Planning committee	4 wks	Fri 15/02/13	Thu 14/03/13
50	Planning decision	0 wks	Thu 14/03/13	Thu 14/03/13
51	Prepare draft Orders	20 wks	Fri 25/05/12	Thu 11/10/12
52	Publish draft Orders	0 wks	Thu 11/10/12	Thu 11/10/12
53	Objection period	12 wks	Fri 12/10/12	Thu 17/01/13
54	Preparation for Public Inquiry	36 wks	Fri 12/10/12	Thu 04/07/13
55	Public Inquiry	4 wks	Fri 05/07/13	Thu 01/08/13
56	Inspector's Report	12 wks	Fri 02/08/13	Thu 24/10/13
57	Preparation of submission for Conditional Approval	8 wks	Fri 13/09/13	Thu 07/11/13
58	Submit MSBC for Conditional Approval	0 wks	Thu 07/11/13	Thu 07/11/13
59	OGC Gateway 3	2 wks	Fri 11/10/13	Thu 24/10/13
60	DfT Consideration	12 wks	Fri 08/11/13	Thu 30/01/14
61	DfT Conditional Approval (SoS Decision)	0 wks	Thu 30/01/14	Thu 30/01/14
62	High Court Challenge Period	6 wks	Fri 31/01/14	Thu 13/03/14
63	Preparation of submission for Final Approval	2 wks	Fri 28/02/14	Thu 13/03/14
64	Submit MSBC for Final Approval	0 wks	Thu 19/06/14	Thu 19/06/14
65	DfT Consideration	4 wks	Fri 20/06/14	Thu 17/07/14
66	DfT Final Approval	0 wks	Thu 17/07/14	Thu 17/07/14
67	Cabinet approval to proceed to construction	4 wks	Fri 18/07/14	Thu 14/08/14
68	Notice to Proceed to Construction	0 wks	Thu 14/08/14	Thu 14/08/14
69	**Detailed Design and Construction**	**128 wks**	**Fri 15/08/14**	**Thu 26/01/17**
70	Detailed design	36 wks	Fri 15/08/14	Thu 23/04/15
71	Land entry notice period	3 wks	Fri 10/10/14	Thu 30/10/14
72	Construction period	104 wks	Fri 30/01/15	Thu 26/01/17
73	OGC Gateway 4	2 wks	Fri 13/01/17	Thu 26/01/17
74	Link open	0 wks	Thu 26/01/17	Thu 26/01/17

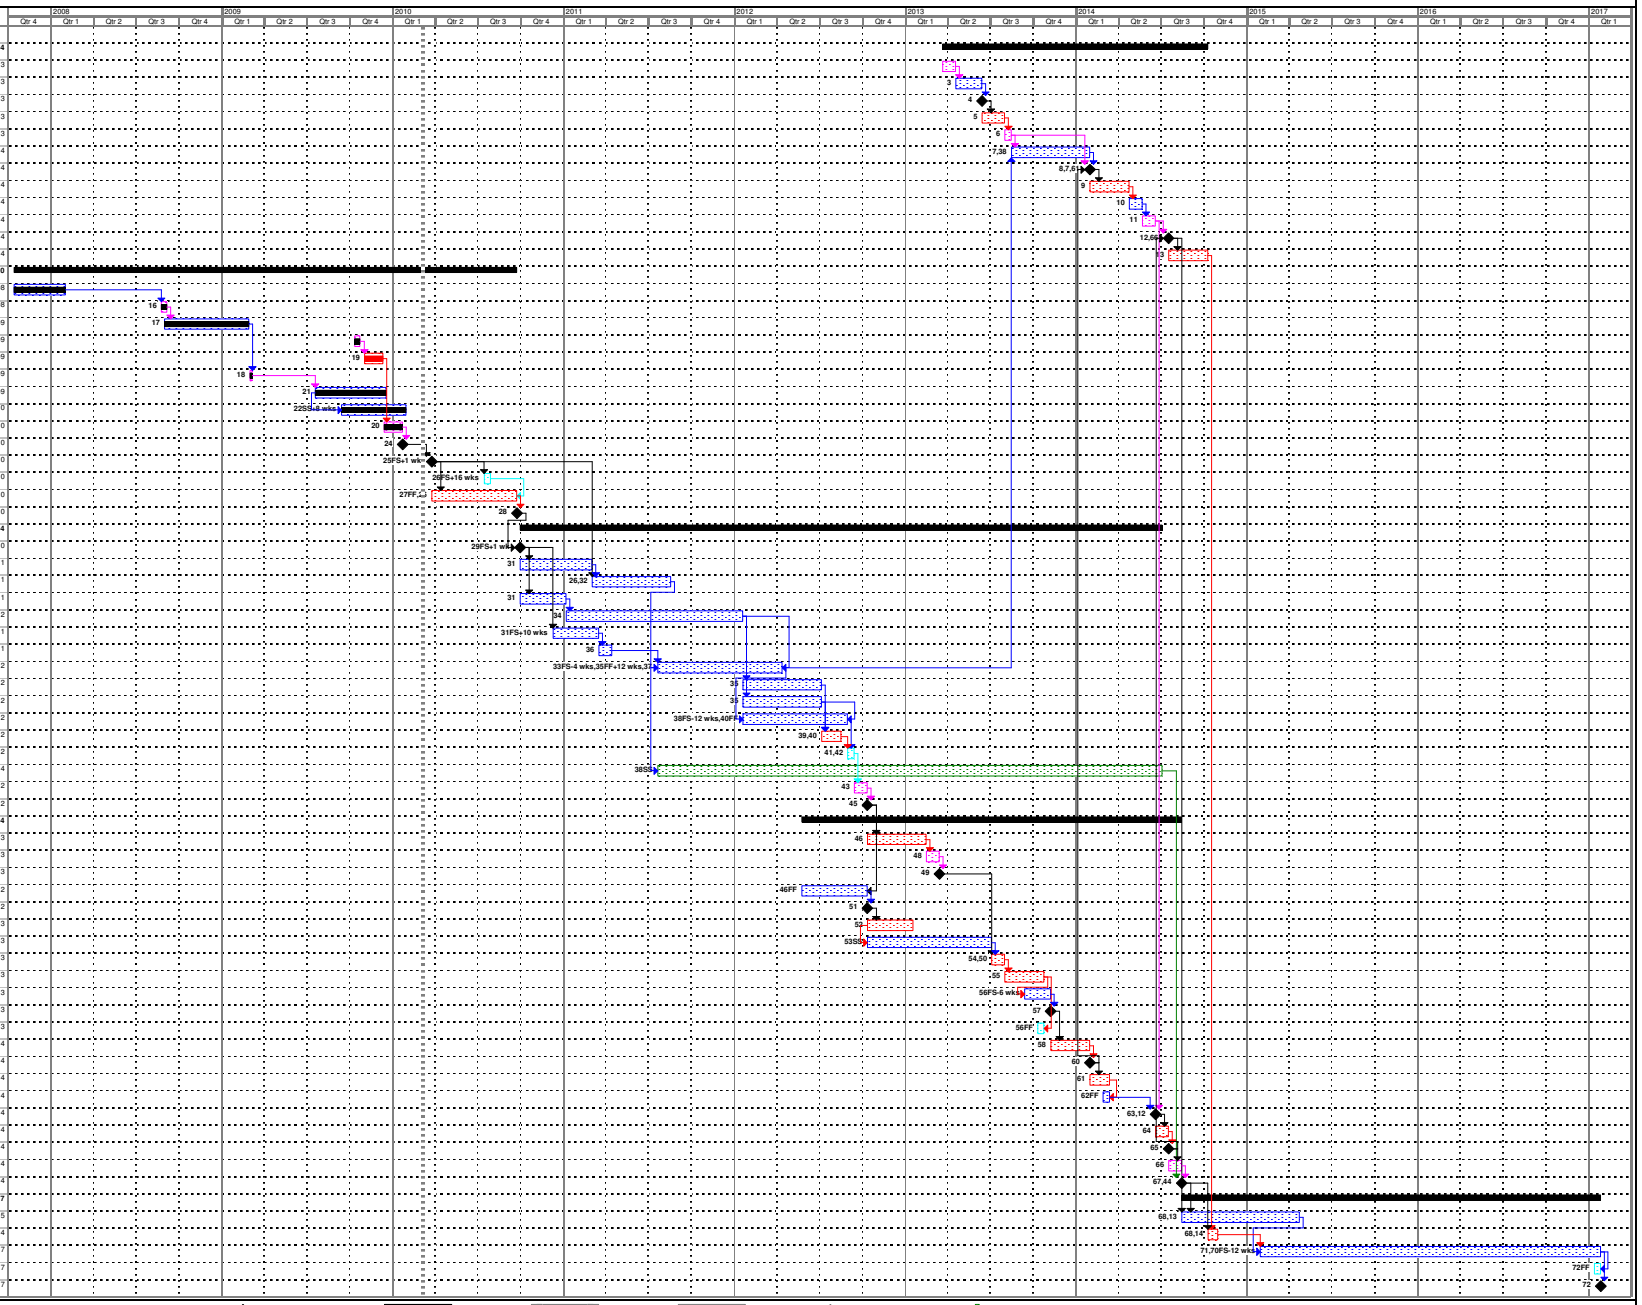

Project: Overall programme Rev 6f - D
Date: Fri 05/03/10

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
